EIA Project Plan for Goedemoed Vineyard, Robertson Western Cape

Project Start: Wed, 25/06/2025

Display Week: 1

TASK	ASSIGNED TO	PROGRESS	START	END	DAYS
Biodiversity Assessment	RVS	100%	25-Jun-2025	6-Jul-2025	12
Agricultural Soil Assessment	RVS	100%	25-Jun-2025	6-Jul-2025	12
Watercourse and Wetland Assessment	RVS	100%	25-Jun-2025	6-Jul-2025	12
Screening Phase and/or Pre-Application Meeting	CL	100%	7-Jul-2025	8-Jul-2025	2
Draft Scoping Report	RVS	80%	9-Jul-2025	22-Aug-2025	45
Exclude: Unavailable	CL	0%	25-Aug-2025	7-Sep-2025	
PPP1: Notification Phase / Registration of I&	PPP	0%	10-Sep-2025	30-Sep-2025	**21**
Submit Application Form / NIT	CL	0%	1-Oct-2025	14-Oct-2025	**14**
PPP2: Comment on Draft Scoping Report	PPP	0%	1-Oct-2025	30-Oct-2025	**30**
* Finalise Scoping Report for Submission	CL	0%	31-Oct-2025	1-Nov-2025	2
CA: Accept/Reject of FSR	DEADP	0%	2-Nov-2025	14-Dec-2025	**43**
Exclude Timeframe	CL	0%	15-Dec-2025	5-Jan-2026	22
Draft EIA Report and EMP	RVS	0%	5-Jan-2026	7-Mar-2026	62
PPP 3: Comment on Draft EIA and EMP Rep	PPP	0%	16-Mar-2026	14-Apr-2026	**30**
Finalise EIA Report and EMP for Submission	CL	0%	15-Apr-2026	28-Apr-2026	14
CA: Decision - Environmental Authorisatior	DEADP	0%	29-Apr-2026	13-Aug-2026	**107**
Notification of Decision	CL	0%	13-Aug-2026	26-Aug-2026	**14**



KEY:

- **Scoping & EIA**
- **Public Participation**
- **Exclude / Unavailable**
- **Specialists**

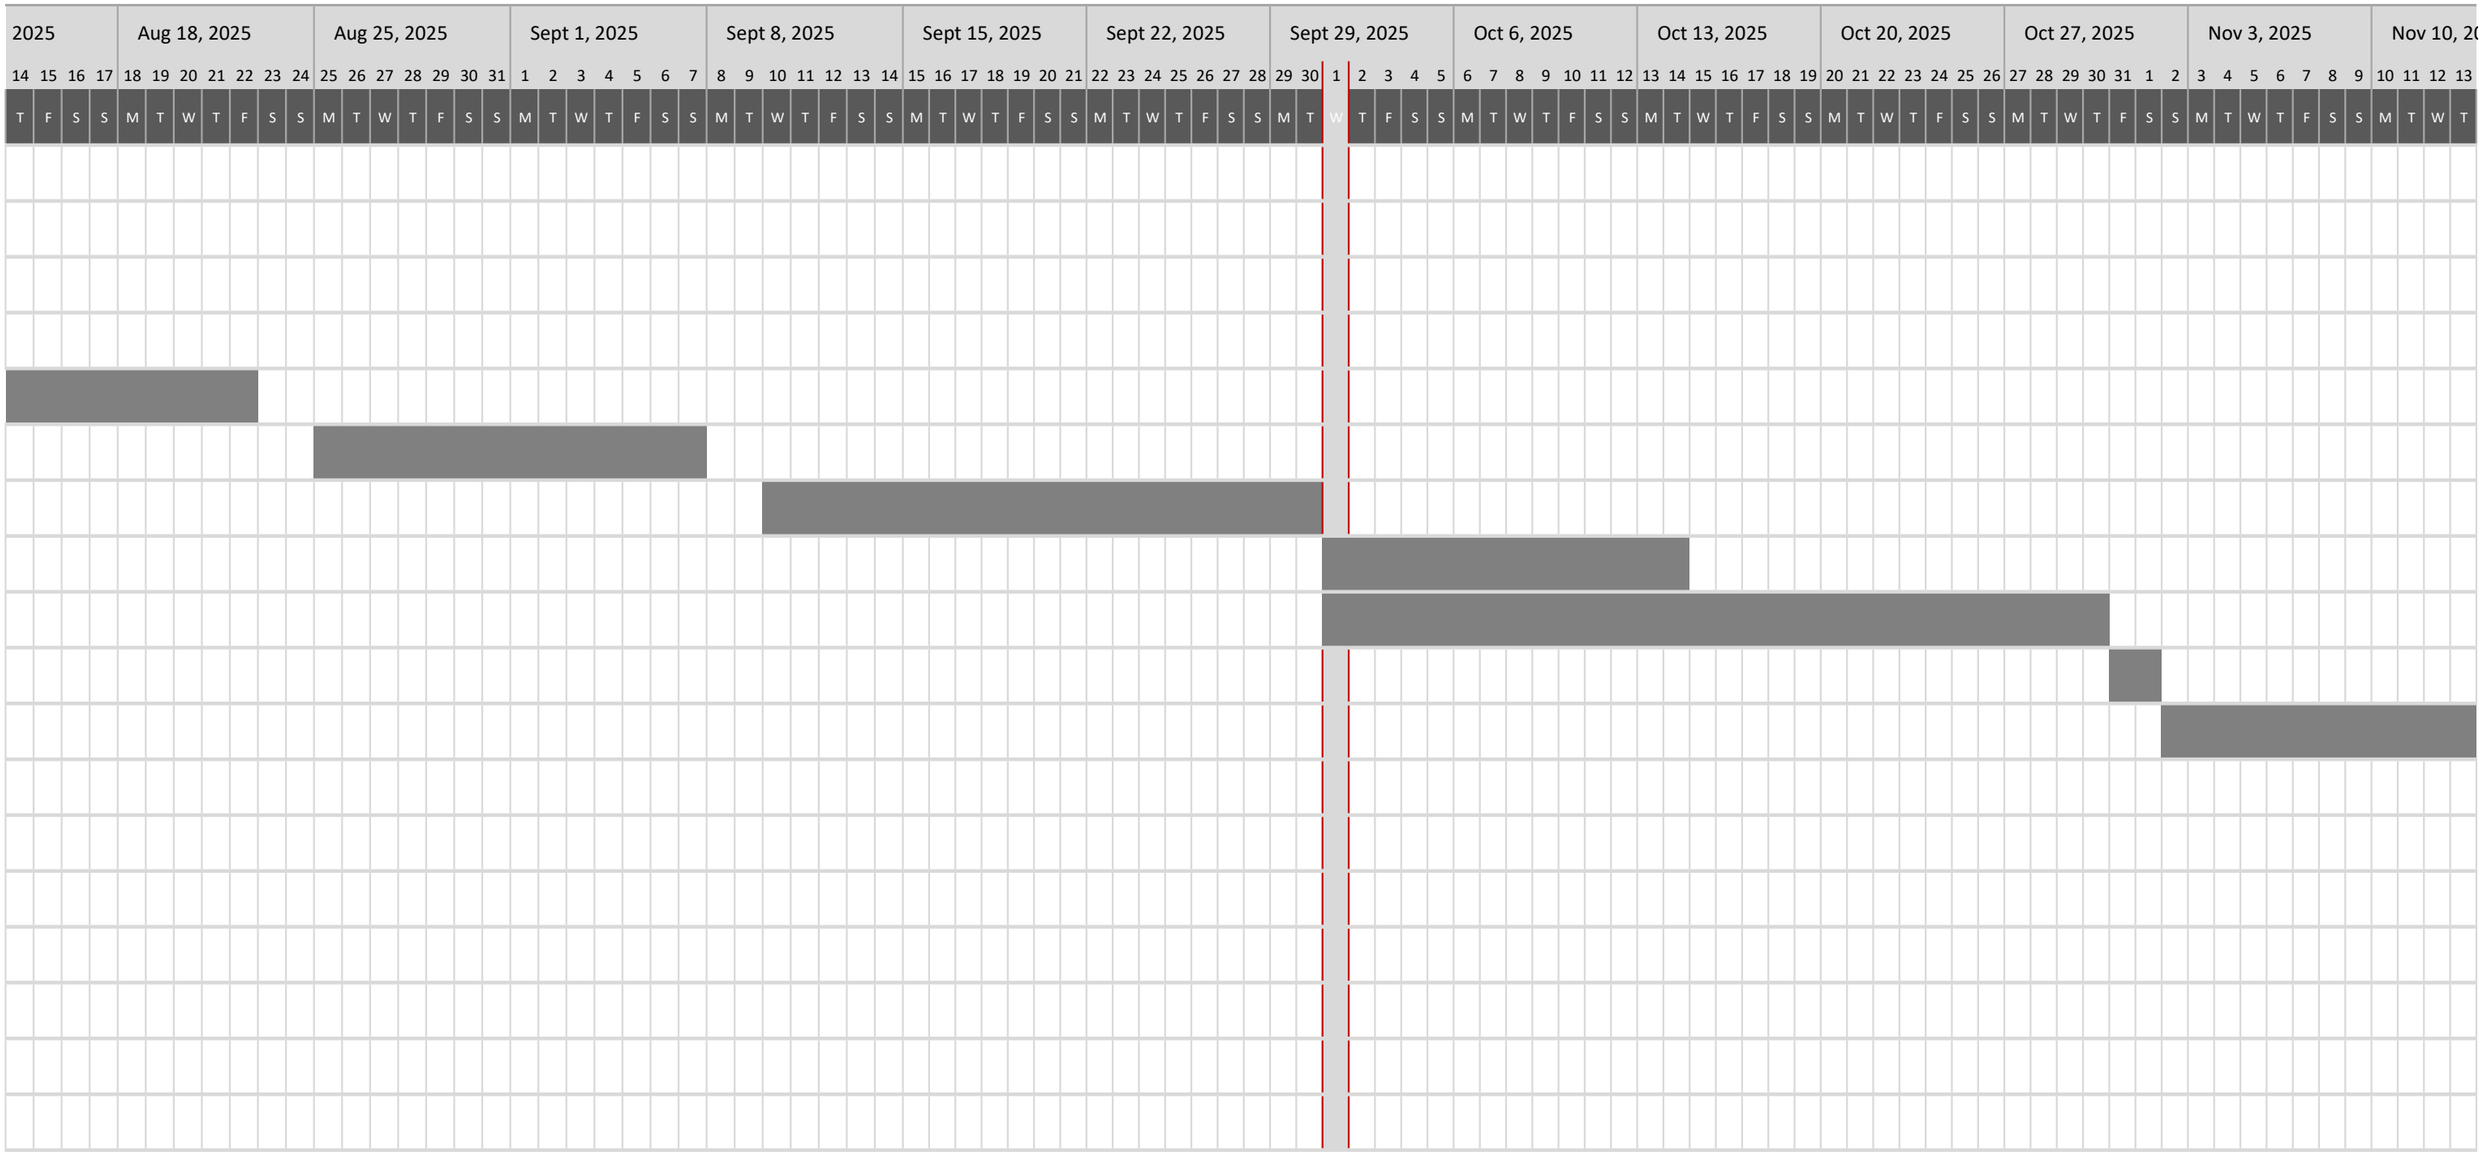
2025
Aug 18, 2025
Aug 25, 2025
Sept 1, 2025
Sept 8, 2025
Sept 15, 2025
Sept 22, 2025
Sept 29, 2025
Oct 6, 2025
Oct 13, 2025
Oct 20, 2025
Oct 27, 2025
Nov 3, 2025
Nov 10, 20
14 15 16 17 18 19 20 21 22 23 24 25 26 27 28 29 30 31 1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23 24 25 26 27 28 29 30 1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23 24 25 26 27 28 29 30 31 1 2 3 4 5 6 7 8 9 10 11 12 13
T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T

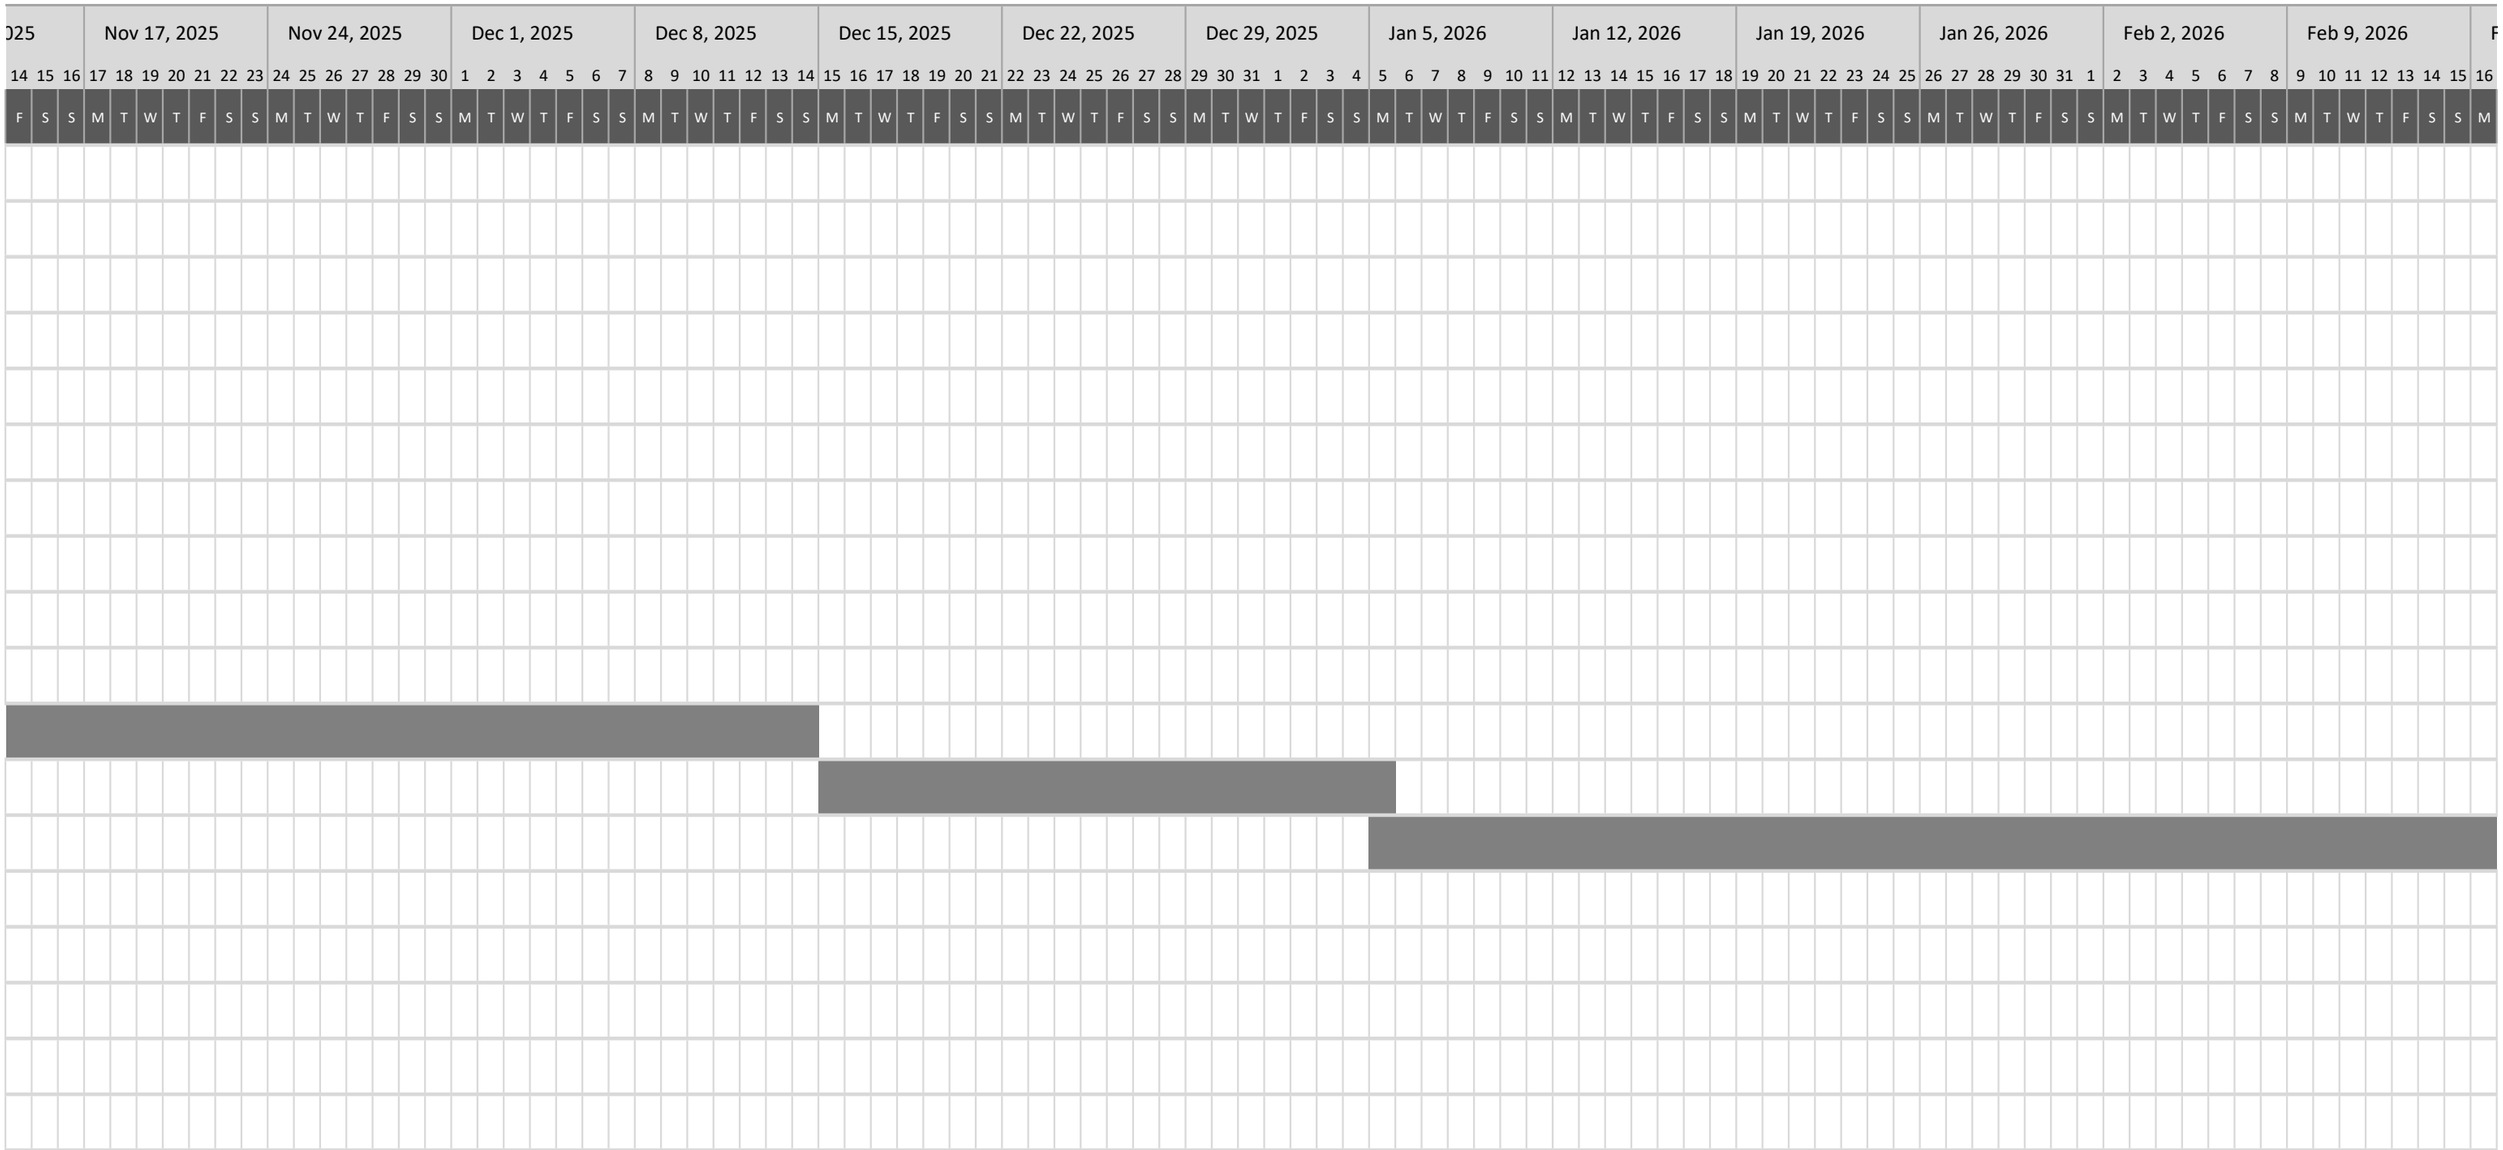
025
Nov 17, 2025
Nov 24, 2025
Dec 1, 2025
Dec 8, 2025
Dec 15, 2025
Dec 22, 2025
Dec 29, 2025
Jan 5, 2026
Jan 12, 2026
Jan 19, 2026
Jan 26, 2026
Feb 2, 2026
Feb 9, 2026
14 15 16 17 18 19 20 21 22 23 24 25 26 27 28 29 30 1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23 24 25 26 27 28 29 30 31 1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23 24 25 26 27 28 29 30 31 1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16
F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M

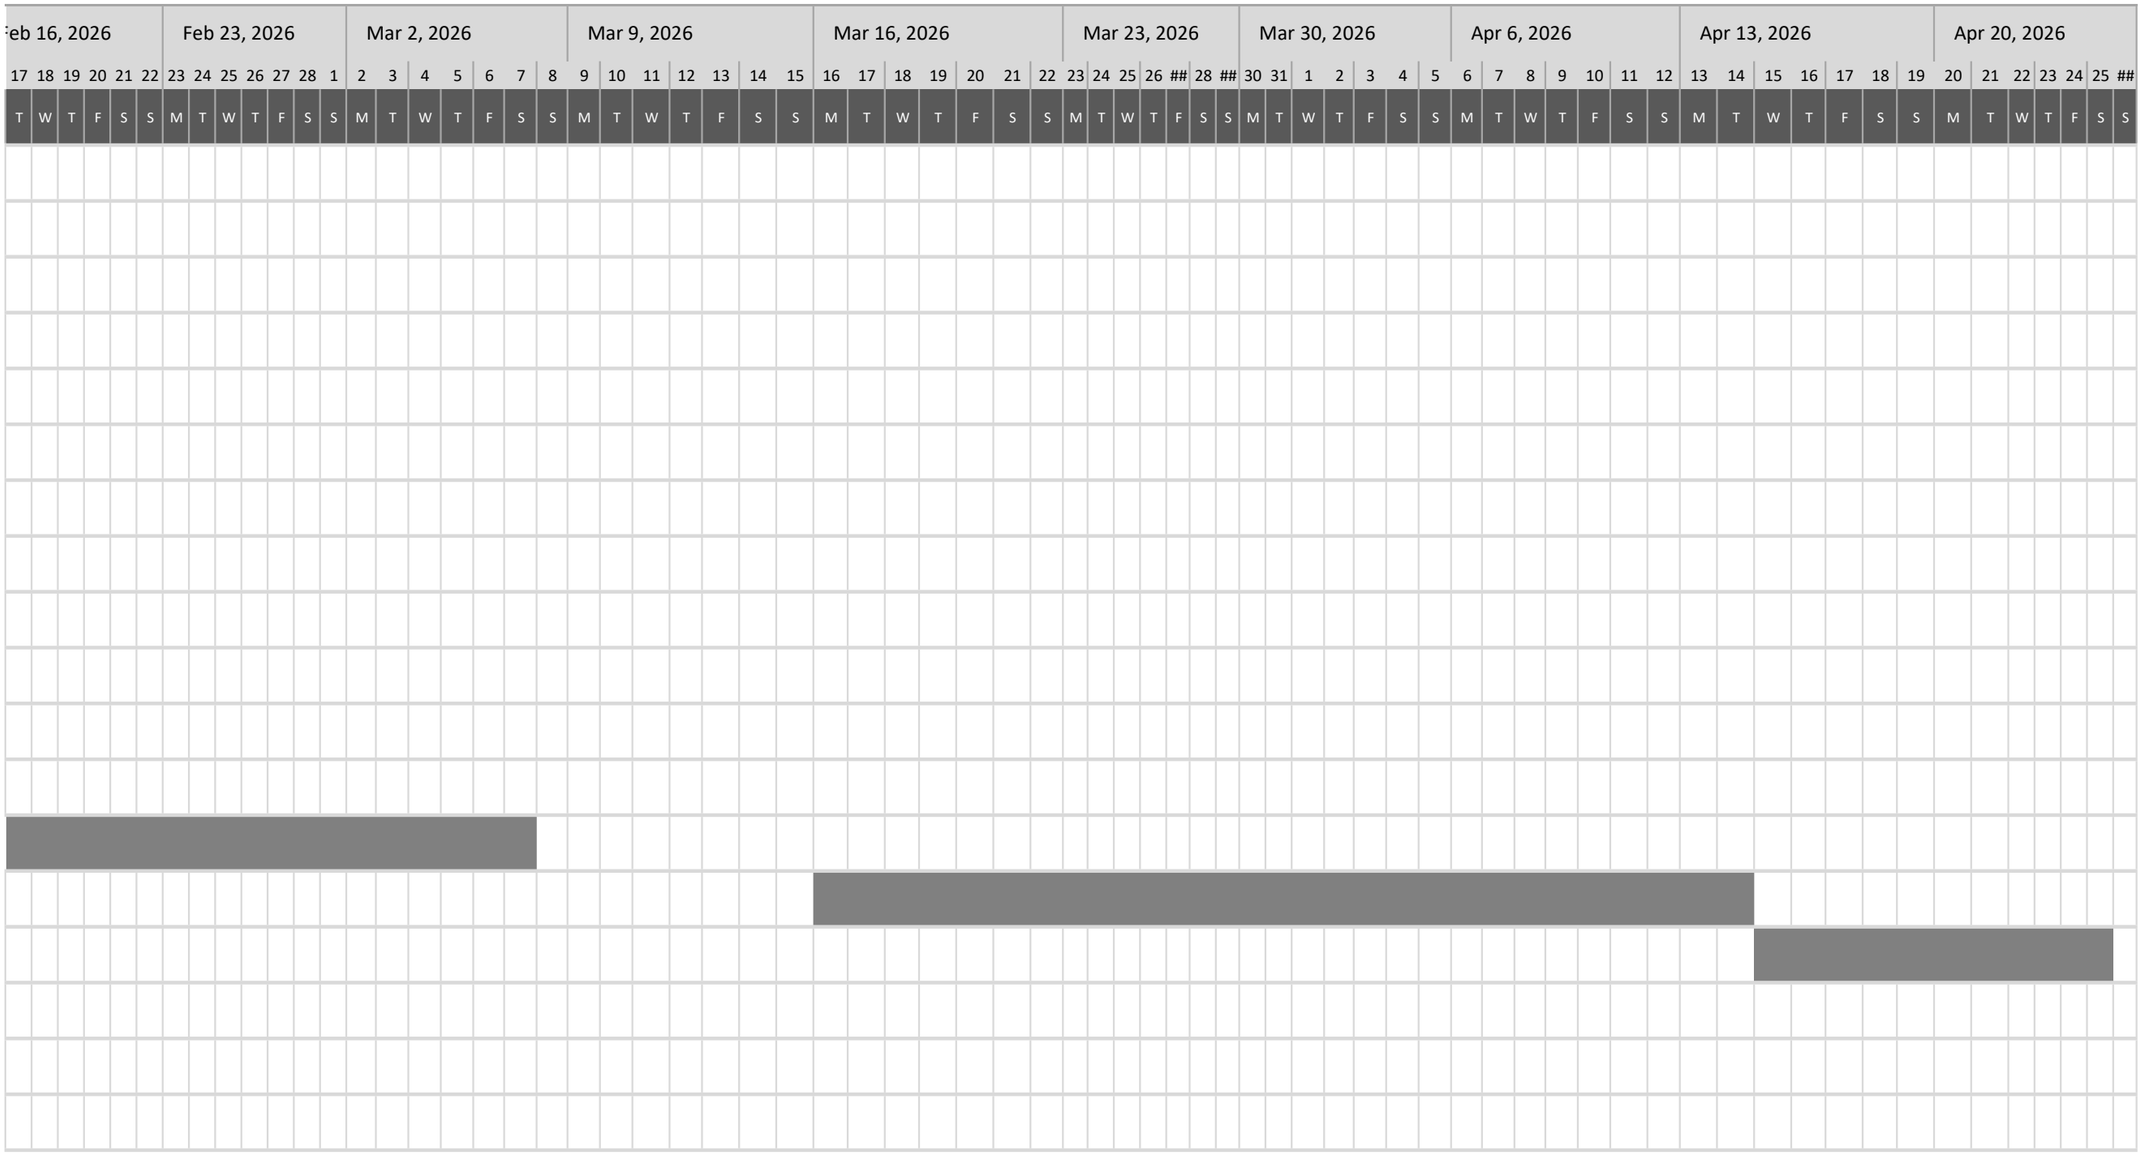
eb 16, 2026
Feb 23, 2026
Mar 2, 2026
Mar 9, 2026
Mar 16, 2026
Mar 23, 2026
Mar 30, 2026
Apr 6, 2026
Apr 13, 2026
Apr 20, 2026
17 18 19 20 21 22 23 24 25 26 27 28 1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23 24 25 26 ## 28 ## 30 31 1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23 24 25 ##
T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S
